

SE LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Problem Statement #46 — Remote Team Time-Tracking & Project Approver

Name: Anjanaa Vijaysankar

SRN: PES1UG24CS654

1. Jira Backlog — Epics & User Stories

Remote Time Tracker							
Ask AI Search work AV Filter Group							
	Work	Assignee	Reporter	Priority	Status	Resolution	Created
	SL2-7 Epic 1: Time Logging & Tracking	Unassigned	AV Anjanaa Vijaysa...	Medium	To Do	Unresolved	Aug 28, 2026, 2:41 PM
	SL2-12 Story 1.3: Validate Jira Task Link	Unassigned	AV Anjanaa Vijaysa...	High	In Review	Unresolved	Aug 28, 2026, 2:44 PM
	SL2-11 Story 1.2: Daily Hour Cap Validation	Unassigned	AV Anjanaa Vijaysa...	High	In Review	Unresolved	Aug 28, 2026, 2:44 PM
	SL2-13 Story 1.4: View Timesheet Status	Unassigned	AV Anjanaa Vijaysa...	Medium	In Review	Unresolved	Aug 28, 2026, 2:45 PM
	SL2-10 Story 1.1: Log Time Entry	Unassigned	AV Anjanaa Vijaysa...	High	In Review	Unresolved	Aug 28, 2026, 2:44 PM
	SL2-8 Epic 2: Timesheet Approval Workflow	Unassigned	AV Anjanaa Vijaysa...	Medium	To Do	Unresolved	Aug 28, 2026, 2:42 PM
	SL2-16 Story 2.3: Approve Timesheet	Unassigned	AV Anjanaa Vijaysa...	High	To Do	Unresolved	Aug 28, 2026, 2:46 PM
	SL2-14 Story 2.1: Submit Timesheet for Approval	Unassigned	AV Anjanaa Vijaysa...	High	In Review	Unresolved	Aug 28, 2026, 2:46 PM
	SL2-15 Story 2.2: Review Timesheet	Unassigned	AV Anjanaa Vijaysa...	High	In Review	Unresolved	Aug 28, 2026, 2:46 PM
	SL2-17 Story 2.4: Reject Timesheet	Unassigned	AV Anjanaa Vijaysa...	High	In Review	Unresolved	Aug 28, 2026, 2:47 PM
	SL2-9 Epic 3: Budget Monitoring & Alerts	Unassigned	AV Anjanaa Vijaysa...	Medium	To Do	Unresolved	Aug 28, 2026, 2:42 PM
	SL2-18 Story 3.1: View Project Budget Burn	Unassigned	AV Anjanaa Vijaysa...	High	Done	Done	Aug 28, 2026, 2:48 PM
	SL2-19 Story 3.2: Real-Time Dashboard Updates	Unassigned	AV Anjanaa Vijaysa...	High	Done	Done	Aug 28, 2026, 2:48 PM
+ Create 3 of 3							

2. Story Point Assignments

Spaces

Remote Time Tracker

...

Summary

List

Board

Backlog

Development

Forms

Timeline

Docs

Reports

+

Q Search backlog

AV

Filter

...

SL2 Sprint 1

28 Aug – 4 Sep (8 work items)

1800

Complete sprint

...

Deliver end-to-end time logging and manager approval workflow

SL2-10

Story 1.1: Log Time Entry

Epic 1: Time Loggi...

To Do

3

...

SL2-11

Story 1.2: Daily Hour Cap Validation

Epic 1: Time Loggi...

To Do

2

...

SL2-12

Story 1.3: Validate Jira Task Link

Epic 1: Time Loggi...

To Do

3

...

SL2-13

Story 1.4: View Timesheet Status

Epic 1: Time Loggi...

To Do

1

...

SL2-14

Story 2.1: Submit Timesheet for Approval

Epic 2: Timesheet ...

To Do

3

...

SL2-15

Story 2.2: Review Timesheet

Epic 2: Timesheet ...

To Do

2

...

SL2-16

Story 2.3: Approve Timesheet

Epic 2: Timesheet ...

To Do

2

...

SL2-17

Story 2.4: Reject Timesheet

Epic 2: Timesheet ...

To Do

2

...

+ Create

Backlog (2 work items)

1000

Create sprint

...

SL2-18

Story 3.1: View Project Budget Burn

Epic 3: Budget Mo...

To Do

5

...

SL2-19

Story 3.2: Real-Time Dashboard Updates

Epic 3: Budget Mo...

To Do

5

...

+ Create

3. Sprint Board — Active Sprint View

Spaces

Remote Time Tracker

...

Summary

List

Board

Backlog

Development

Forms

Timeline

Docs

Reports

+

Q Search board

AV

Filter

Group

Complete sprint

...

To Do 5

Story 1.1: Log Time Entry

Parent

Epic 1: Time Logging & Tracking

SL2-10

3

...

Story 1.2: Daily Hour Cap Validation

Parent

Epic 1: Time Logging & Tracking

SL2-11

2

...

Story 1.4: View Timesheet Status

Parent

Epic 1: Time Logging & Tracking

SL2-13

1

...

Story 2.2: Review Timesheet

+ Create

In Progress 3

Story 1.3: Validate Jira Task Link

Parent

Epic 1: Time Logging & Tracking

SL2-12

3

...

Story 2.1: Submit Timesheet for Approval

Parent

Epic 2: Timesheet Approval Workfl...

SL2-14

3

...

Story 2.4: Reject Timesheet

Parent

Epic 2: Timesheet Approval Workfl...

SL2-17

2

...


+ Create

In Review 0


+ Create


Done 0

+ Create

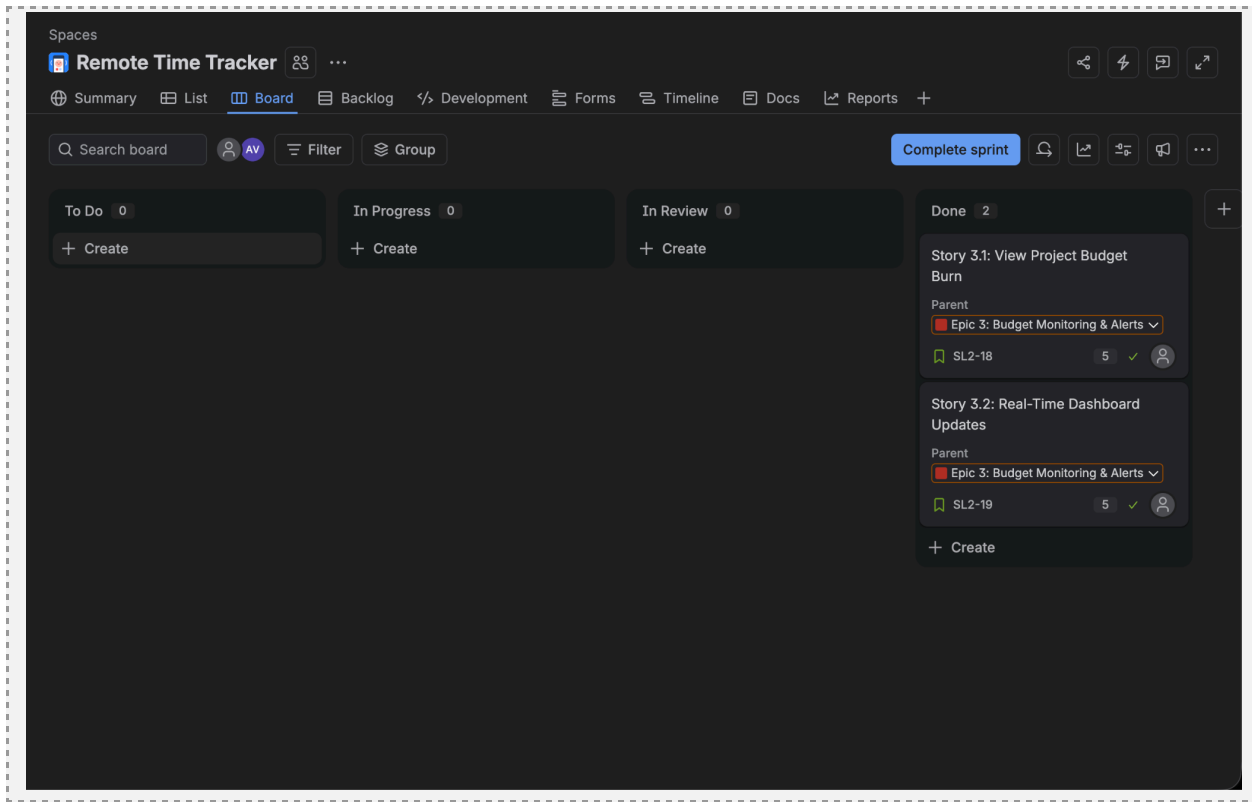

4. Burndown Chart

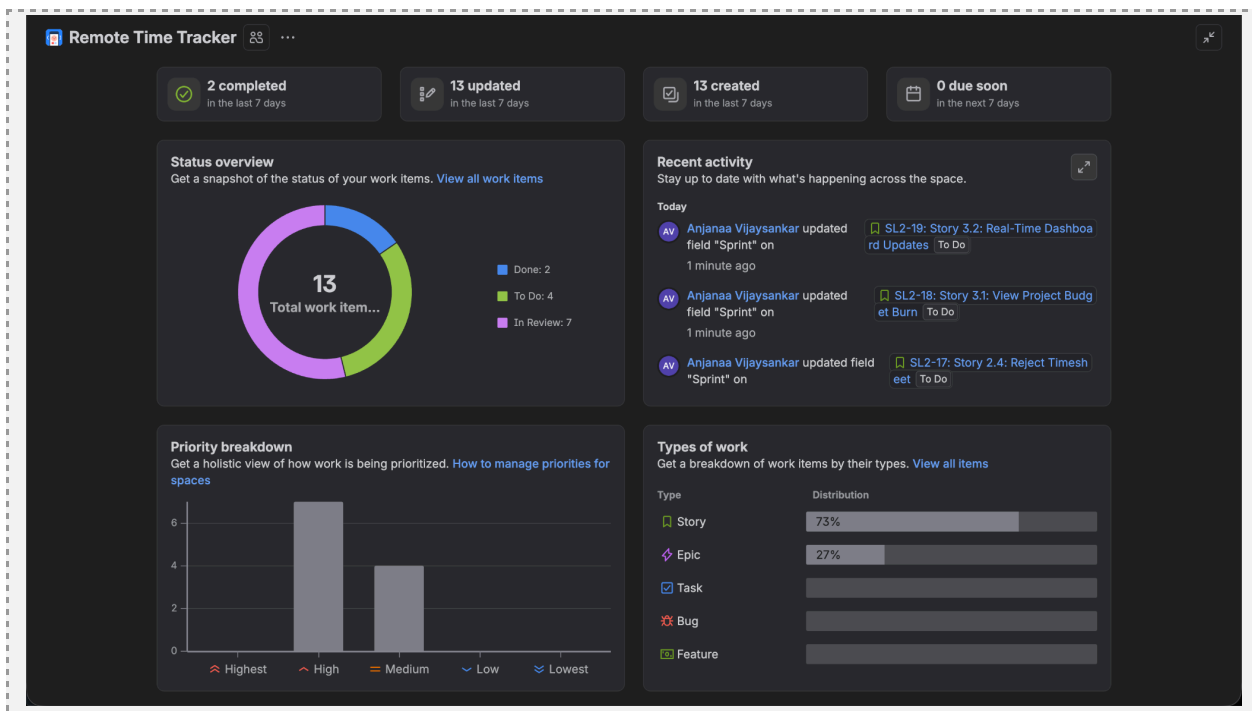

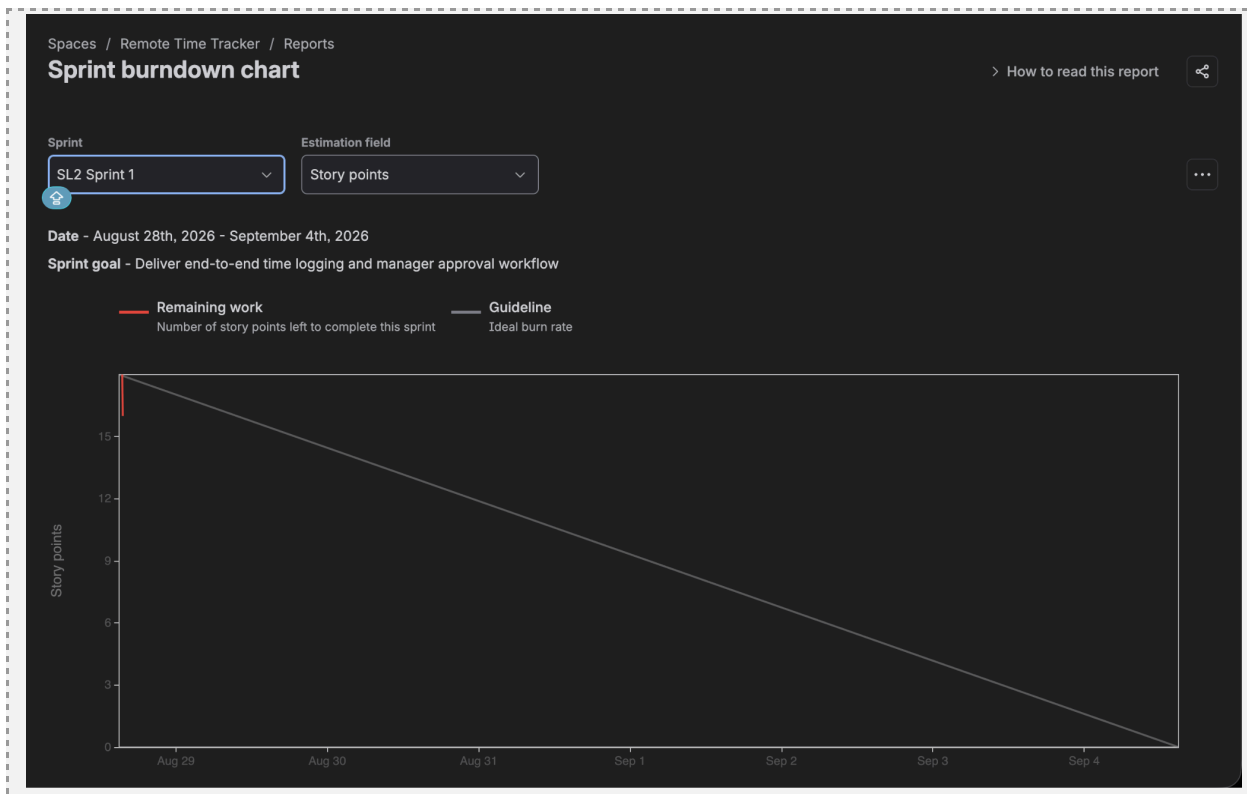

5. Reflection Questions

1. Did your estimations reflect the actual effort?

For the most part, yes. Simple stories like viewing timesheet status (1 pt) and the approve/reject actions (2 pts) matched their low complexity, while stories involving validation logic (Daily Hour Cap, Jira Task Link — 2-3 pts) and the budget burn calculation with real-time dashboard updates (5 pts each) were rightly estimated higher since they involve business-rule logic and performance work tied to NFR-001. [Edit this once you've completed the simulated sprint and can compare planned vs. actual completion.]

2. Was your backlog well-prioritized?

Yes. Priorities were derived directly from the Lab 1 requirements table — FR-001, FR-002, FR-003, FR-004 and FR-005 are all High priority, so their corresponding stories (time logging, hour-cap validation, task linking, submission, review, approval, rejection, and budget burn) were kept High. The one exception is 'View Timesheet Status' (Medium), which is a convenience feature for developers rather than a core requirement tied to an FR.

3. How did your simulated sprint align with your plan?

Sprint 1 was scoped to deliver one complete, demonstrable workflow end-to-end — a developer logging and submitting time, and a manager reviewing, approving, or rejecting it (Epics 1 and 2, 18 points). Sprint 2 focused solely on the budget-monitoring capability (Epic 3, 10 points), which logically depends on approved hours existing from Sprint 1. This ordering meant each sprint produced a usable increment rather than half-finished features spread across both epics.

4. What insights did the burndown chart give about your team's capacity?

[Fill this in after viewing your actual burndown chart.] Note whether the remaining-work line tracked close to the ideal guideline line (steady, predictable progress), finished early/late, or dropped sharply at one point (which would suggest a story was larger than its point estimate, e.g. the budget burn calculation).
